


LARP

LARP Phase II Quick Update

7th Sep. 2009



- Jaw mandrel for second jaw has been successfully brazed and now at external vendor for machining. Next step is machining and brazing outer jaw surfaces. Mandrel currently at outside mandrel for machining.
- Current design work concentrating on vacuum chamber and BPM
- Most parts have been ordered for final SPS test assembly, the rest to be ordered soon
- Other than small technical details, only pending issue foreseen at this time: Will ferrite be required to damp trapped modes (studies in progress)?
- Detailed update for the past several months and future plans is intended to be given at next meeting.



LARP


Mandrel winding completed and brazed



Winding



Brazing results:
looks good

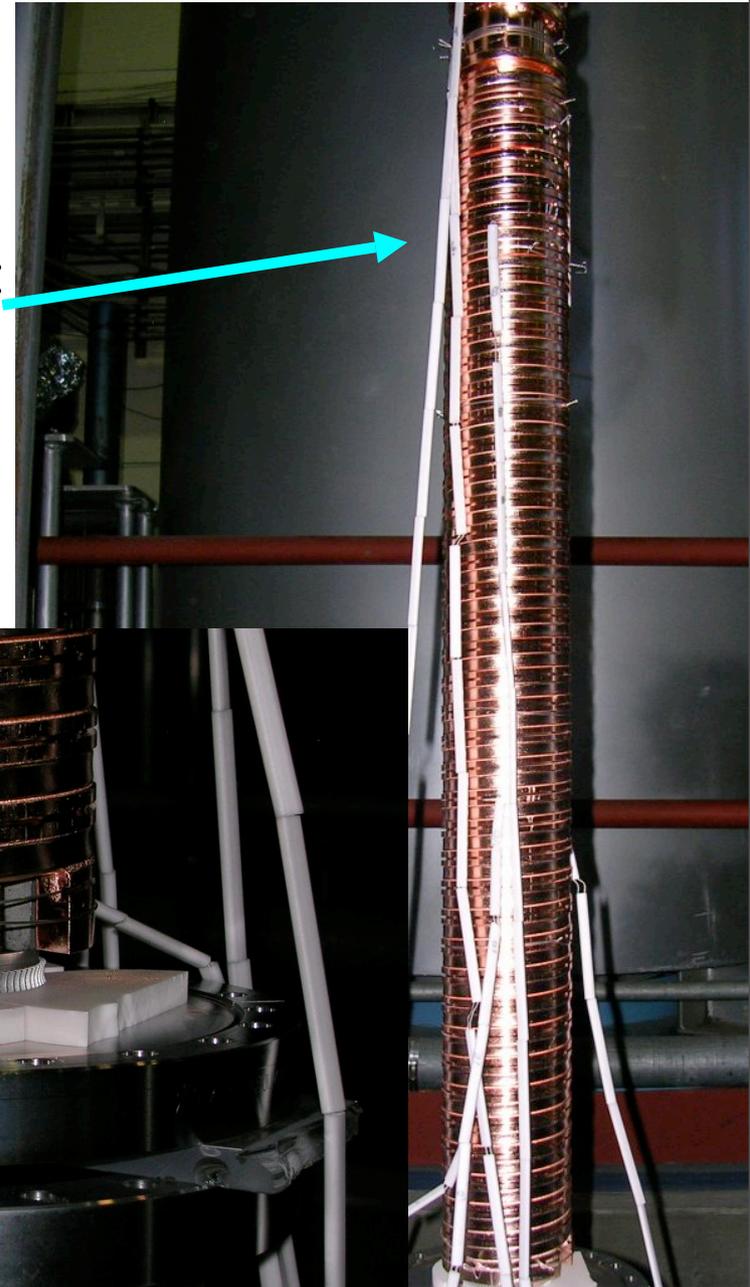

Braze
prep.

